

Greenhaven/Pierson



Storm Drainage Improvement Project

February 6, 2018



Project Status

Construction is ahead of schedule and expected to be complete by May 2018.

Construction highlights

- Construction continues to progress along Greenhaven Lane.
- Pipes have been installed from Pierson pond up Greenhaven Lane to the intersection of Winfield Drive. Curb and gutter is currently being installed on this same stretch.
- Water and sewer line relocations have been completed at the intersection of Greenhaven Lane and Pierson Drive as well as Greenhaven Lane and Winfield Drive.
- B&N Grading, Inc. continue to install the 48-inch pipe system up Winfield Drive and new curb and gutter along Winfield Drive until the end of February.
- Construction along Pierson Drive to Winfield Drive is expected to begin in early March.



For more information

Harold Smith, Project Manager
HSmith@CharlotteNC.gov
704-432-5532

Heather Botzko, Construction Inspector
Heather.Botzko@CharlotteNC.gov
704-747-3559


StormWater.CharMeck.org



Engineering & Property Management
Storm Water Services Division
600 East Fourth Street
Charlotte, North Carolina 28202

Investing in Infrastructure

Storm Water Services designs and constructs projects that make a difference in the lives of residents across the city. Our community benefits when stormwater quickly drains off roads, flood risks to homes are reduced and the health of local streams is protected or improved.

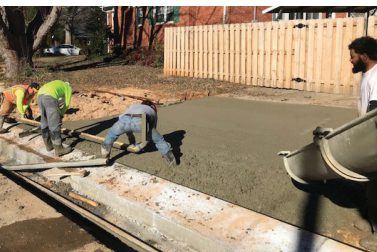

The Greenhaven/Pierson project goal is to reduce street and structure flooding throughout the neighborhood.

StormWater.CharMeck.org
